


Project Reset Report

Project: Amazon Connect Agent Supervisor Insights

Date: February 3, 2026

Team: AWS Minority Business Support 4 (Team 5)

Architecture Diagram

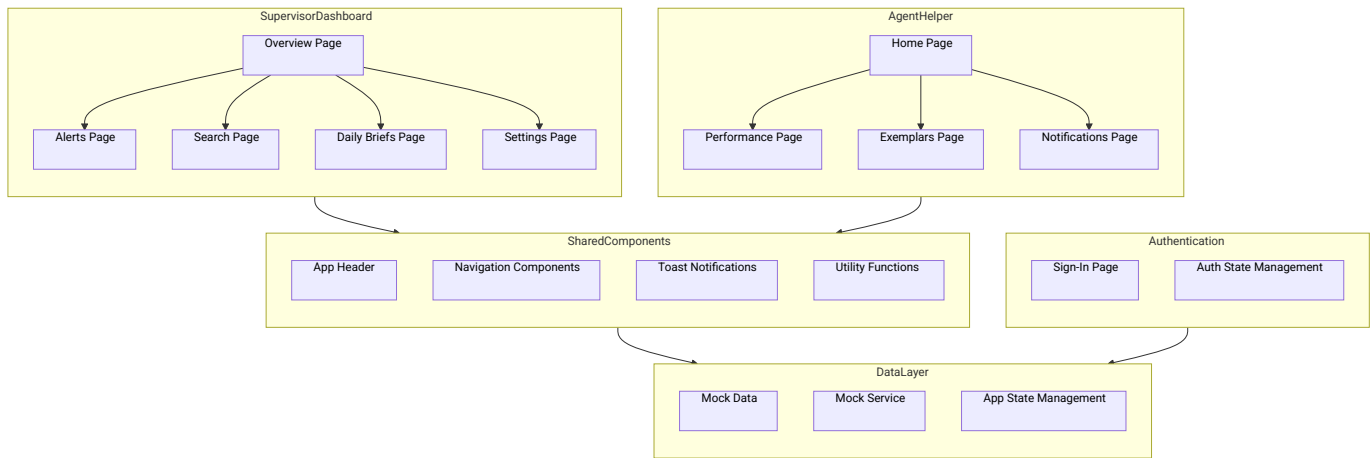

Architecture Explanation

The system is currently a client-only React application with two primary user experiences: a **Supervisor Dashboard** (overview, alerts, search, briefs, settings) and an **Agent Helper** (home, performance, exemplars, notifications). Both areas depend on shared UI components and utilities. State is managed via a centralized app store and auth store, and all data is supplied by a mock data layer (MockData + MockService) that simulates backend behavior. Authentication is also mocked client-side, and data persistence relies on local storage. There is no backend API, service abstraction, or production authentication layer yet, so the end-to-end flow is entirely in-browser.

Technical Debt & Risk List (Summary)

Critical

- **TD-01 Mock-only data layer:** UI is tightly coupled to mock services; no path to real API integration. High impact on backend/production readiness.
- **TD-02 Mock authentication:** Hardcoded users, localStorage sessions, and client-only route guards. High security and compliance risk.
- **TD-03 No automated tests:** Zero test coverage; refactors are unsafe and regressions are likely.

- **R-02 Security & privacy risks:** Unsanitized inputs, localStorage secrets, CSV injection risk, and future PII/AI data leakage concerns.

High

- **TD-04 TypeScript strict mode disabled:** Weak type safety increases runtime error risk and slows refactoring.
- **R-01 AI hallucination risk:** Future AI summaries/coaching require grounding, validation, and human review controls.

Medium

- **TD-05 No CI quality gates:** Lint/build/tests not enforced pre-merge.
- **TD-06 Documentation gaps:** Missing deployment docs, ADRs, business rule rationale, and traceability.
- **R-03 Vendor lock-in:** Reliance on AWS + Lovable/shadcn/Radix without abstraction.
- **TD-08 AI-generated code consistency:** Inconsistent patterns, missing edge cases, duplicated logic.

Backlog Health & Readiness Assessment

Evidence of Review

- Issues are broken down by feature epics (F1–F9) with scope, acceptance criteria, and API/UI separation.
- Foundational technical debt items are explicitly tracked (auth, service abstraction, tests).
- Several backlog items include clear, testable acceptance checklists.

Gaps / Risks

- Some issues are missing dependencies or sequencing notes (e.g., backend contracts vs. UI wiring).
- Risk items are documented separately but not consistently linked to backlog items.

Recommendations

- Add priority and sprint fields to issues, and explicitly tag tech debt vs. features.
- Link debt/risk items to the epics they unblock (e.g., TD-01 → all API wiring tasks).
- Add Definition of Ready (DoR) checklist to backlog items: contract defined, acceptance criteria verified, dependencies resolved.

Initial Senior Project II Priorities

1. Establish test foundation (TD-03)

- Set up Vitest + Testing Library, add test scripts, and cover core logic and store behavior.

2. Replace mock auth with secure baseline (TD-02)

- Integrate Cognito/Auth0; move secrets server-side; enforce session expiration and RBAC.

3. Introduce service abstraction layer (TD-01)

- Define service interfaces, refactor mock services, and add API stubs to enable backend integration.

4. Enable TypeScript strictness (TD-04)

- Incrementally enable strict checks and fix high-impact type issues.

5. Add CI quality gates (TD-05)

- Lint/build/test in GitHub Actions and require passing checks before merge.
